Glenside Combined HOP Schedule 070621

PH&C LLC
LAND DEVELOPMENT SERVICES
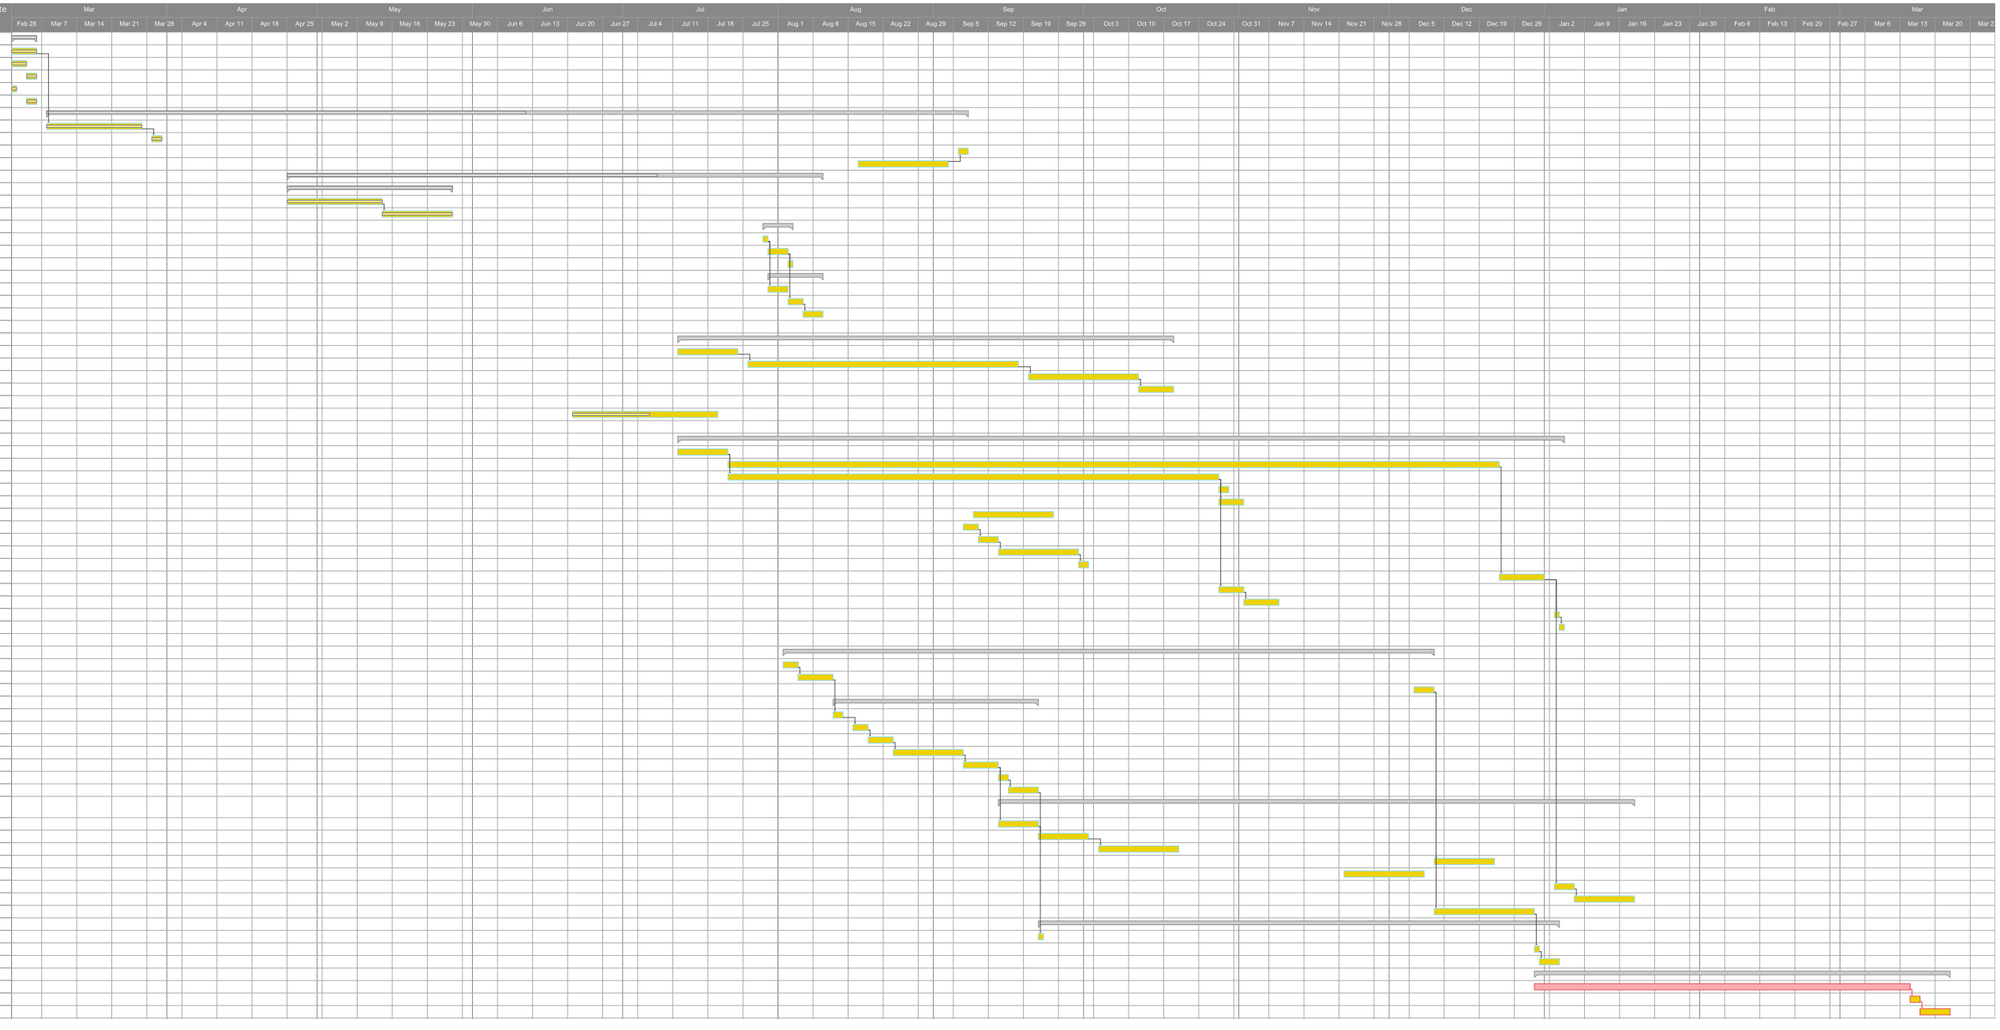
Task Name	Duration	Start	Finish	Predecessors	% Complete
SITE WORK	5d	03/01/21	03/05/21		100%
CLEARING AND EROSION CONTROL	5d	03/01/21	03/05/21		100%
REMOVE FENCING/BRUSH ETC.	3d	03/01/21	03/03/21		100%
REMOVE ASPHALT PAVING	2d	03/04/21	03/05/21		100%
INSTALLATION OF TRACKING PADS	1d	03/01/21	03/01/21		100%
INSTALLATION OF SILT SOCK/E+S APPURTENANCES	2d	03/04/21	03/05/21		100%
EARTHWORK	132d	03/08/21	09/07/21		52%
EXCAVATE BASIN TO EXPORT	15d	03/08/21	03/26/21	2	100%
CUT BALANCE OF SITE TO EXPORT	2d	03/29/21	03/30/21	8	100%
FILLS AND GRADING	2d	09/06/21	09/07/21	11	
BALLAST COLUMNS AT FOUNDATIONS	14d	08/17/21	09/03/21		
SITE UTILITIES	77d	04/25/21	08/09/21		69%
STORM SYSTEM	25d	04/25/21	05/27/21		100%
INSTALL BASIN	15d	04/25/21	05/13/21		100%
CONVEYANCE PIPING AND STRUCTURES - SITE	10d	05/14/21	05/27/21	14	100%
SANITARY	4d	07/29/21	08/03/21		
TIE IN	1d	07/29/21	07/29/21		
CROSSING EASTON ROAD	2d	07/30/21	08/02/21	17	
SITE STUB	1d	08/03/21	08/03/21	18	
WATER SUPPLY	7d	07/30/21	08/09/21		
WET TAPS	2d	07/30/21	08/02/21	17	
CROSSING EASTON ROAD	3d	08/03/21	08/05/21	18	
METER PIT AND SITE STUB	2d	08/06/21	08/09/21	22	
HOP UTILITY - AQUA RELOCATION	71d	07/12/21	10/18/21		
SUBMITTAL PROCESS	10d	07/12/21	07/23/21		
MATERIAL LEAD TIME (6 WEEKS)	40d	07/26/21	09/17/21	26	
RELOCATE MAINS	16d	09/20/21	10/11/21	27	
TRENCH RESTORATION	5d	10/12/21	10/18/21	28	
HOP UTILITY - PECO RELOCATION	21d	06/21/21	07/19/21		53%
HOP SIGNALIZATION	127d	07/12/21	01/04/22		
POLE SPOT (PROJECTED)	8d	07/12/21	07/21/21		
MAST ARM LEAD TIME (20-22 WEEKS)	110d	07/22/21	12/22/21	34	
CONTROLLER CABINET LEAD TIME (12-14 WEEKS)	70d	07/22/21	10/27/21	34	
TEMPORARY SIGNALS	2d	10/28/21	10/29/21	36	
REMOVE EXT. EQUIPMENT	3d	10/28/21	11/01/21	36	
INSTALL TRAFFIC FOUNDATIONS & CONDUITS	12d	09/09/21	09/24/21		
REMOVE EXT. STREET POLES & LIGHTS	3d	09/07/21	09/09/21		
INSTALL NEW WOOD POLES & GUY WIRES	2d	09/10/21	09/13/21	40	
INSTALL LIGHTING FOUNDATIONS & CONDUITS	12d	09/14/21	09/29/21	41	
RE-INSTALL ROADWAY/PED LIGHTS	2d	09/30/21	10/01/21	42	
INSTALL NEW MAST ARMS AND SIGNALS	7d	12/23/21	12/31/21	35	
INSTALL CONTROLLER	3d	10/28/21	11/01/21	36	
INSTALL WIRING	5d	11/02/21	11/08/21	45	
INSTALL SIGNS	1d	01/03/22	01/03/22	44	
FINAL INSPECTION	1d	01/04/22	01/04/22	47	
HOP OFF-SITE WORK	94d	08/02/21	12/09/21		
CONSTRUCTION OF TEMPORARY PEDESTRIAN WALKWAY	3d	08/02/21	08/04/21		
DEMOLITION FOR WORK ON SITE SIDE OF EASTON	5d	08/05/21	08/11/21	51	
DEMOLITION FOR WAVERLY ROAD WIDENING	4d	12/06/21	12/09/21		
HOP DRAINAGE	29d	08/12/21	09/21/21		
SET MANHOLE MH-06	2d	08/12/21	08/13/21	52	
MH-06 - I-08 - I-06B	3d	08/16/21	08/18/21	55	
I-08 - I-07B - I-08A	3d	08/19/21	08/23/21	56	
MH-06 - I-06 - I-05 - I-04 - I-03	10d	08/24/21	09/06/21	57	
I-03 - I-02 - MH-01 - I-01 - TIE-IN EXISTING	5d	09/07/21	09/13/21	58	
MH-06 - I-06C	2d	09/14/21	09/15/21	59	
16 MH-06A - MH-06	4d	09/16/21	09/21/21	60	
CONCRETE/CURBING/SIDEWALK/RAMPS AND ASSOCIATED FLATWORK	91d	09/14/21	01/18/22		
CURB @ SITE FRONTAGE	6d	09/14/21	09/21/21	59	
GRANITE CURBING	8d	09/22/21	10/01/21	63	
SIDEWALK/RAMPS - CONCRETE	12d	10/04/21	10/19/21	64	
WAVERLY WIDENING CONCRETE CURBING AND RAMPS	8d	12/10/21	12/21/21	53	
BRICK PAVER WORK	12d	11/22/21	12/07/21		
CORNERS WHERE MAST ARMS BEING RELOCATED	4d	01/03/22	01/06/22	44	
CORNERS OPPOSITE SITE SIDE COMPLETE	8d	01/07/22	01/18/22	68	
WIDENING OF WAVERLY ROAD	14d	12/10/21	12/29/21	53	
FINAL PAVING	74d	09/22/21	01/03/22		
PERMANENT TRENCH REPAIRS STORM SYSTEM	1d	09/22/21	09/22/21	61	
MILLING	1d	12/30/21	12/30/21	70	
OVERLAY	2d	12/31/21	01/03/22	73	
PRESUMED ASPHALT PLANT SHUT DOWN	59d	12/30/21	03/22/22		
ALTERNATE IF ASPHALT PLANT SHUT DOWN	53d	12/30/21	03/14/22		
ALTERNATE MILLING	2d	03/15/22	03/16/22	76	
ALTERNATE OVERLAY	4d	03/17/22	03/22/22	77
